














Activity & Testing Detail - Progress

Monday, June 19th, 2023


ACTIVITY DETAIL DATE SWP & SUBMERSIBLE CAMPAIGN

	Activities	Duration (Day/'s)	Area	Plan Start	Plan Finish	Actual Start	Actual Finish	Remarks
	1 Equipment Un-Preservation	1	According Plan	18 June 23	18 June 23	18 June 23	18 June 23	Done (According Scope of SWP Campaign)
	2 Electric Integrity Test (Pre-Power up Power Generation	1	C/D	19 June 23	19 June 23			
	3 Portable Genset Set-up	1	M/D	18 June 23	18 June 23	18 June 23	-	Remaining Install Cable Control for F&G Detection (Install ACB at Switchgear Inc.3, Sensing VT, Synchroscope) - Continued
	4 All Pumps Venting Check	1	M/D - C/D	18 June 23	18 June 23	18 June 23	18 June 23	Done (traced line, need tubing 25 m, elbow 6 ea, union 5 ea, 3/4" , reducer 1"
	5 SWP-B Installation	1	SC/D	19 June 23	20 June 23			SWP-B Installation Waiting Engineering TQ
	6 Submersible Pump Installation	1	SC/D	19 June 23	20 June 23	19 June 23	19 June 23	Completed
	7 Testing SWP - B of Machinery and Control System	2	SC/D	21 June 23	23 June 23			See at SWP-B Installation
	8 Testing Submersible Pump of Machinery and Control System	1	SC/D	21 June 23	22 June 23			
	9 DEG flame detector (changeover cpy's to vendor's)	1	C/D	19 June 23	19 June 23			Series with Testing SWP-B (Cooling System)
	10 Exercise Cooling System SWP	1	SC/D - C/D	19 June 23	19 June 23			
	11 Synchronization Diesel Generator Installation and Testing.	1	C/D	20 June 23	21 June 23			
	12 Analyze & Observe of Pumps Venting Header to recheck line sizing sufficient.	1	M/D - C/D	18 June 23	18 June 23	18 June 23	-	Traced line, need tubing 25 m, elbow 6 ea, union 5 ea, 3/4" , reducer 1" - Waiting reroute plot plan Drawing

Punch List	Description	Status	Remarks/Result
HVAC	Software	Open	Will be Install at Onshore
DEG	Software	Open	Will be Install at Onshore
GCP (Gas Conditioning Package)	Software	Open	Will be Install at Onshore
SWP A & SWP B	Malfunction	Open	On Progress Rectify (SWP - B will be test at Offshore on SWP Campaign) - Waiting Approval TQ from Engineering
Exit Light At MCC Room	Malfunction	Open	Will be Install at Offshore
DEG-PMS	Permissive/ESD to Start DEG (NC -> NO)	Open	Will be rectify at Offshore

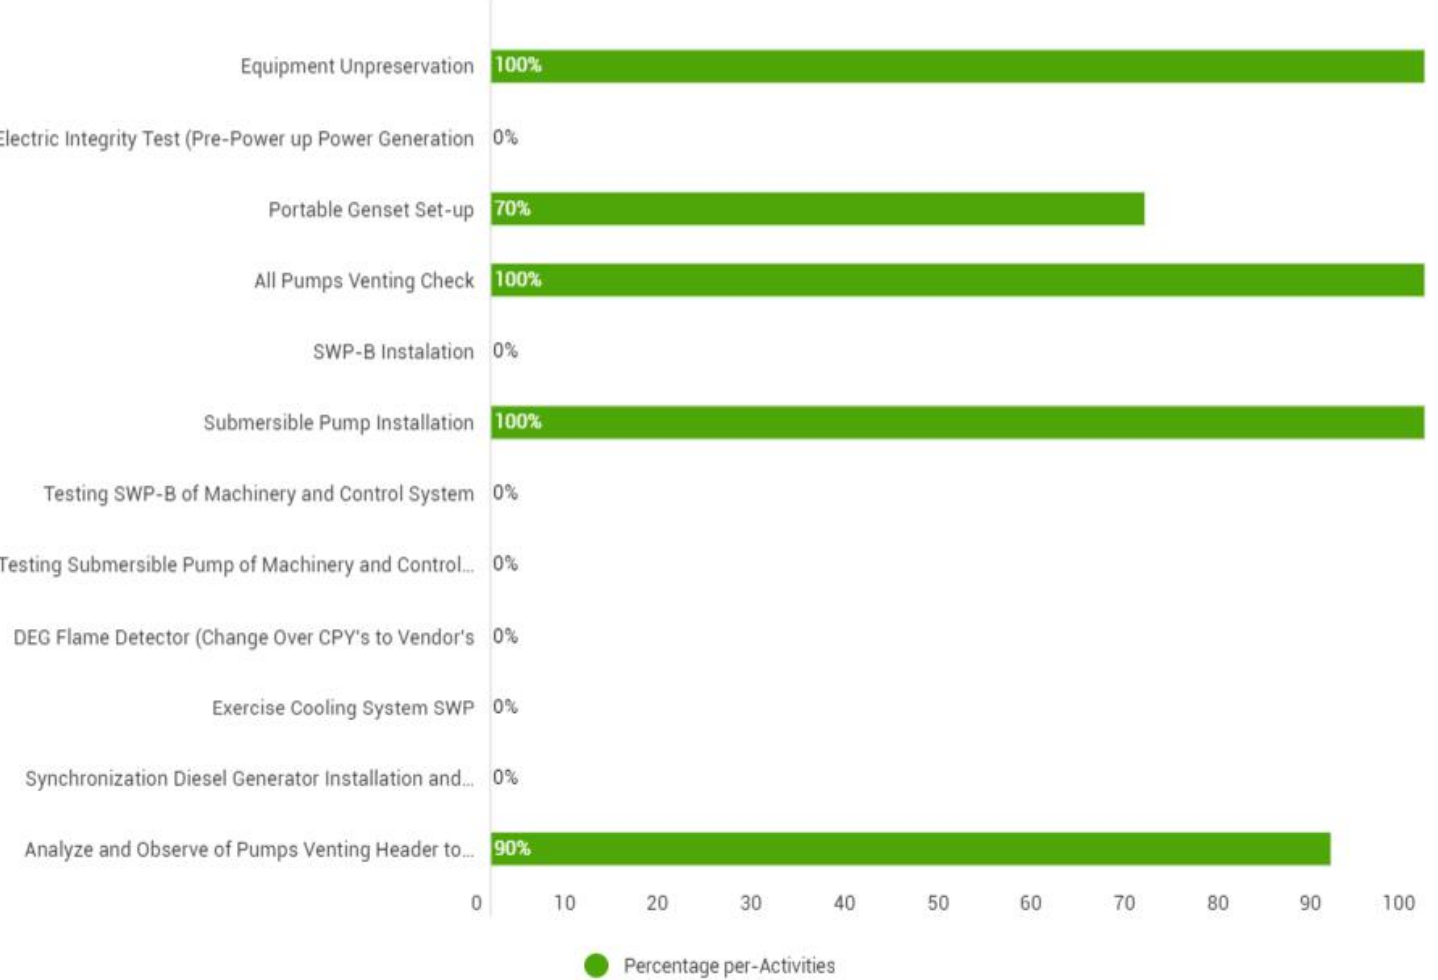

OVERALL PERCENTAGE

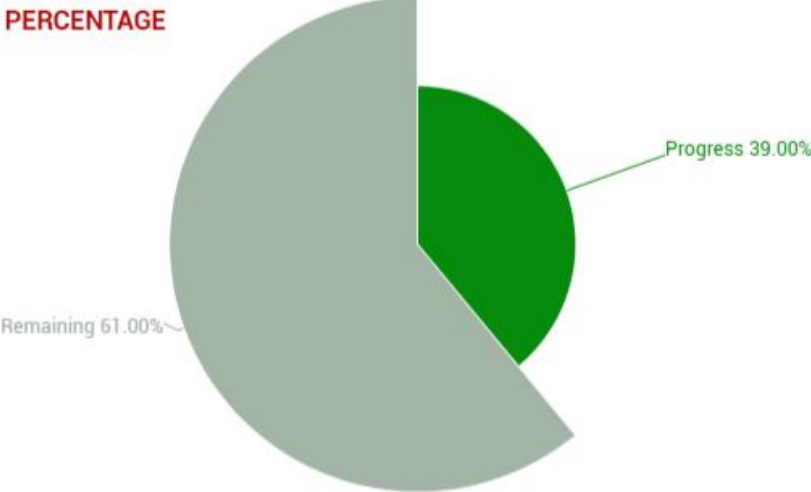

OVERALL PERCENTAGE FOR ACTIVITY & TESTING SWP CAMPAIGN JUNE 17th, 2023 - JUNE 24th, 2023
