
Page 6 of 6 Download


## Activity & Testing Detail - Progress

Thursday, June 22th, 2023

## ACTIVITY DETAIL DATE SWP & SUBMERSIBLE CAMPAIGN

		Activities	Duration (Day/'s)	Area	Plan Start	Plan Finish	Actual Start	Actual Finish	Remarks
	1	Equipment Un-Preservation	1	According Plan	18 June 23	18 June 23	18 June 23	18 June 23	COMPLETED (According Scope of SWP Campaign)
	2	Electric Integrity Test (Pre- Power up Power Generation	1	C/D	19 June 23	19 June 23	20 June 23	20 June 23	COMPLETED
	3	Portable Genset Set-up	1	M/D	18 June 23`	18 June 23	18 June 23	20 June 23	COMPLETED
	4	All Pumps Venting Check	1	M/D - C/D	18 June 23	18 June 23	18 June 23	18 June 23	COMPLETED
	5	SWP-B Installation	1	SC/D	19 June 23	20 June 23	21 June 23	22 June 23	COMPLETED - the minute of meeting on 20 June 2023 became the basis for SWP-B installation - remaining installation are discharge head, motor stool, and motor alignment
	6	Submersible Pump Installation	1	SC/D	19 June 23	20 June 23	19 June 23	19 June 23	COMPLETED
لمافالهالها	7	Testing SWP - B of Machinery and Control System	2	SC/D	21 June 23	23 June 23	22 June 23	-	Plan Start Mech - Run 22 June 2023 at 19:00
	8	Testing Submersible Pump of Machinery and Control System	1	SC/D	21 June 23	22 June 23	20 June 23	21 June 23	COMPLETED - Actual Finish 21 June 2023 at 10:00 AM)
	9	DEG flame detector (changeover cpy's to vendor's)	1	C/D	19 June 23	19 June 23	22 June 23	22 June 23	COMPLETED - because the actual item arrived at the site on June 21, 2023 at 22:00
	10	Exercise Cooling System SWP	1	SC/D - C/D	19 June 23	19 June 23	22 June 23	-	Plan Start Mech - Run With Cooling 22 June 2023 at 18:30
	11	Synchronization Diesel Generator Installation and Testing.	1	C/D	20 June 23	21 June 23	21 June 23	22 June 23	COMPLETED
	12	Analyze & Observe of Pumps Venting Header to recheck line sizing	1	M/D - C/D	18 June 23	18 June 23	18 June 23	20 June 23	COMPLETED - Traced line, need tubing 25 m, elbow 6 ea, union 5 ea, 3/4", reducer 1" - reroute plot plan Drawing (Done)

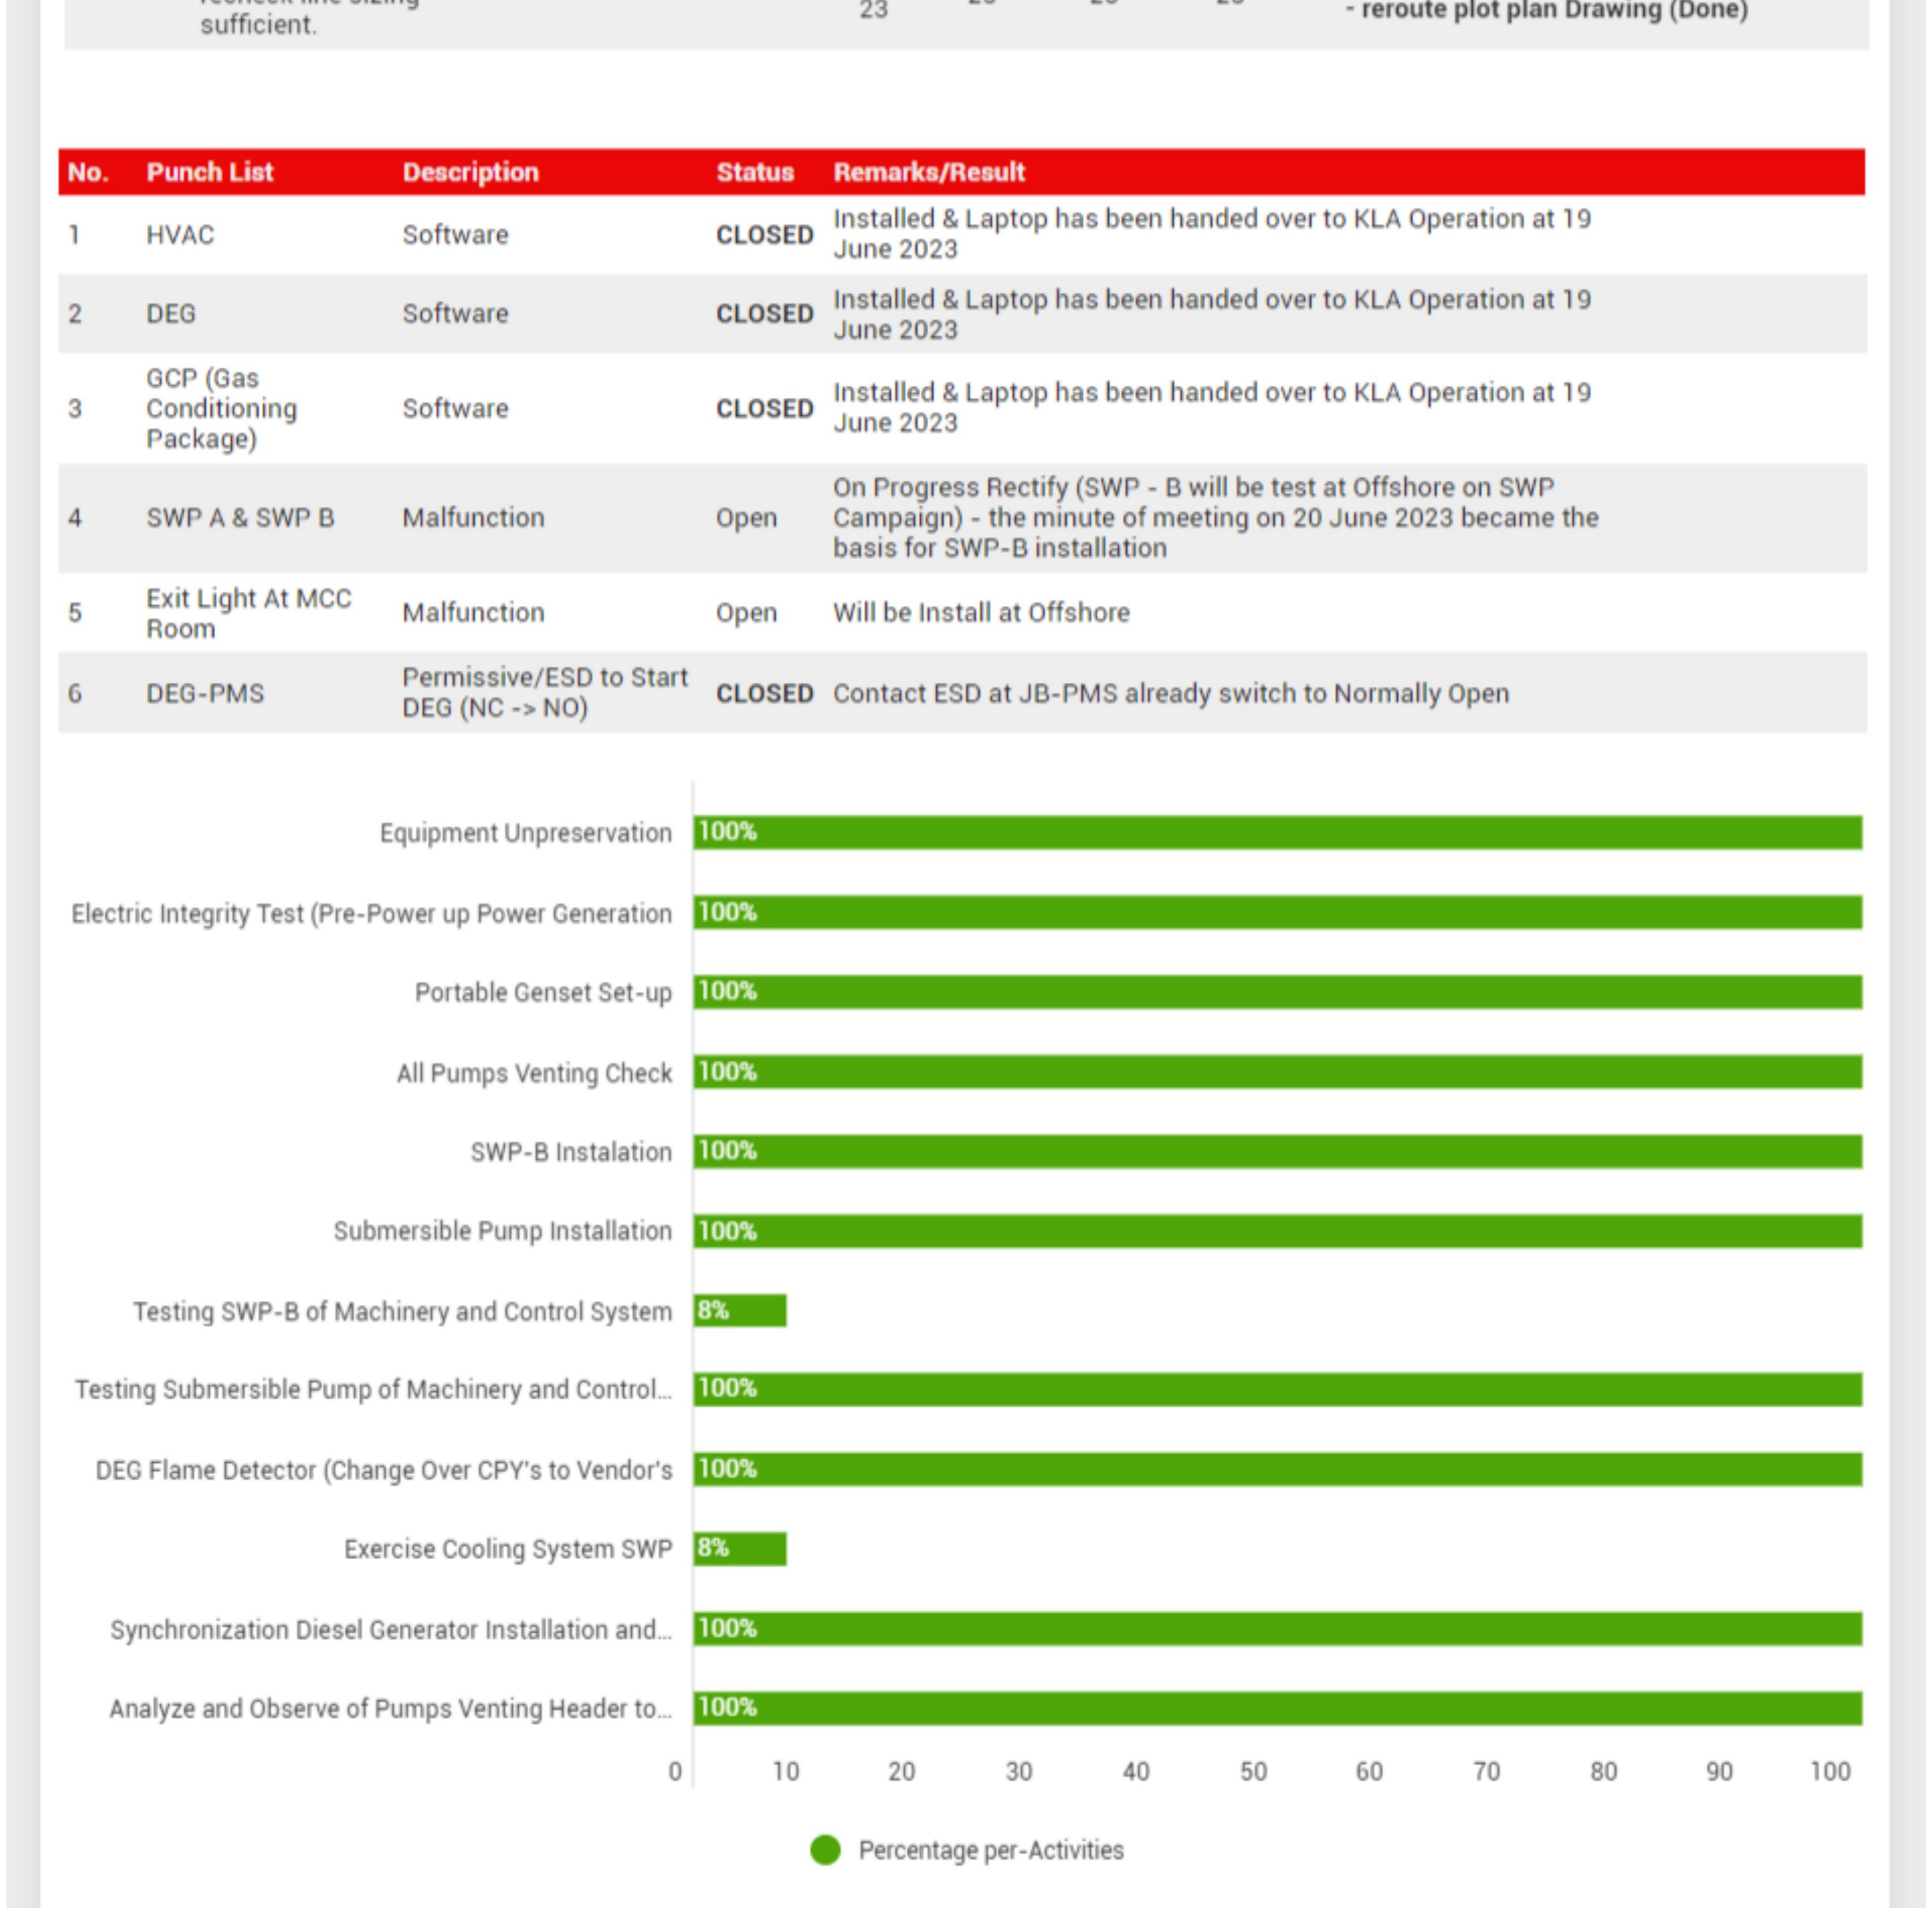

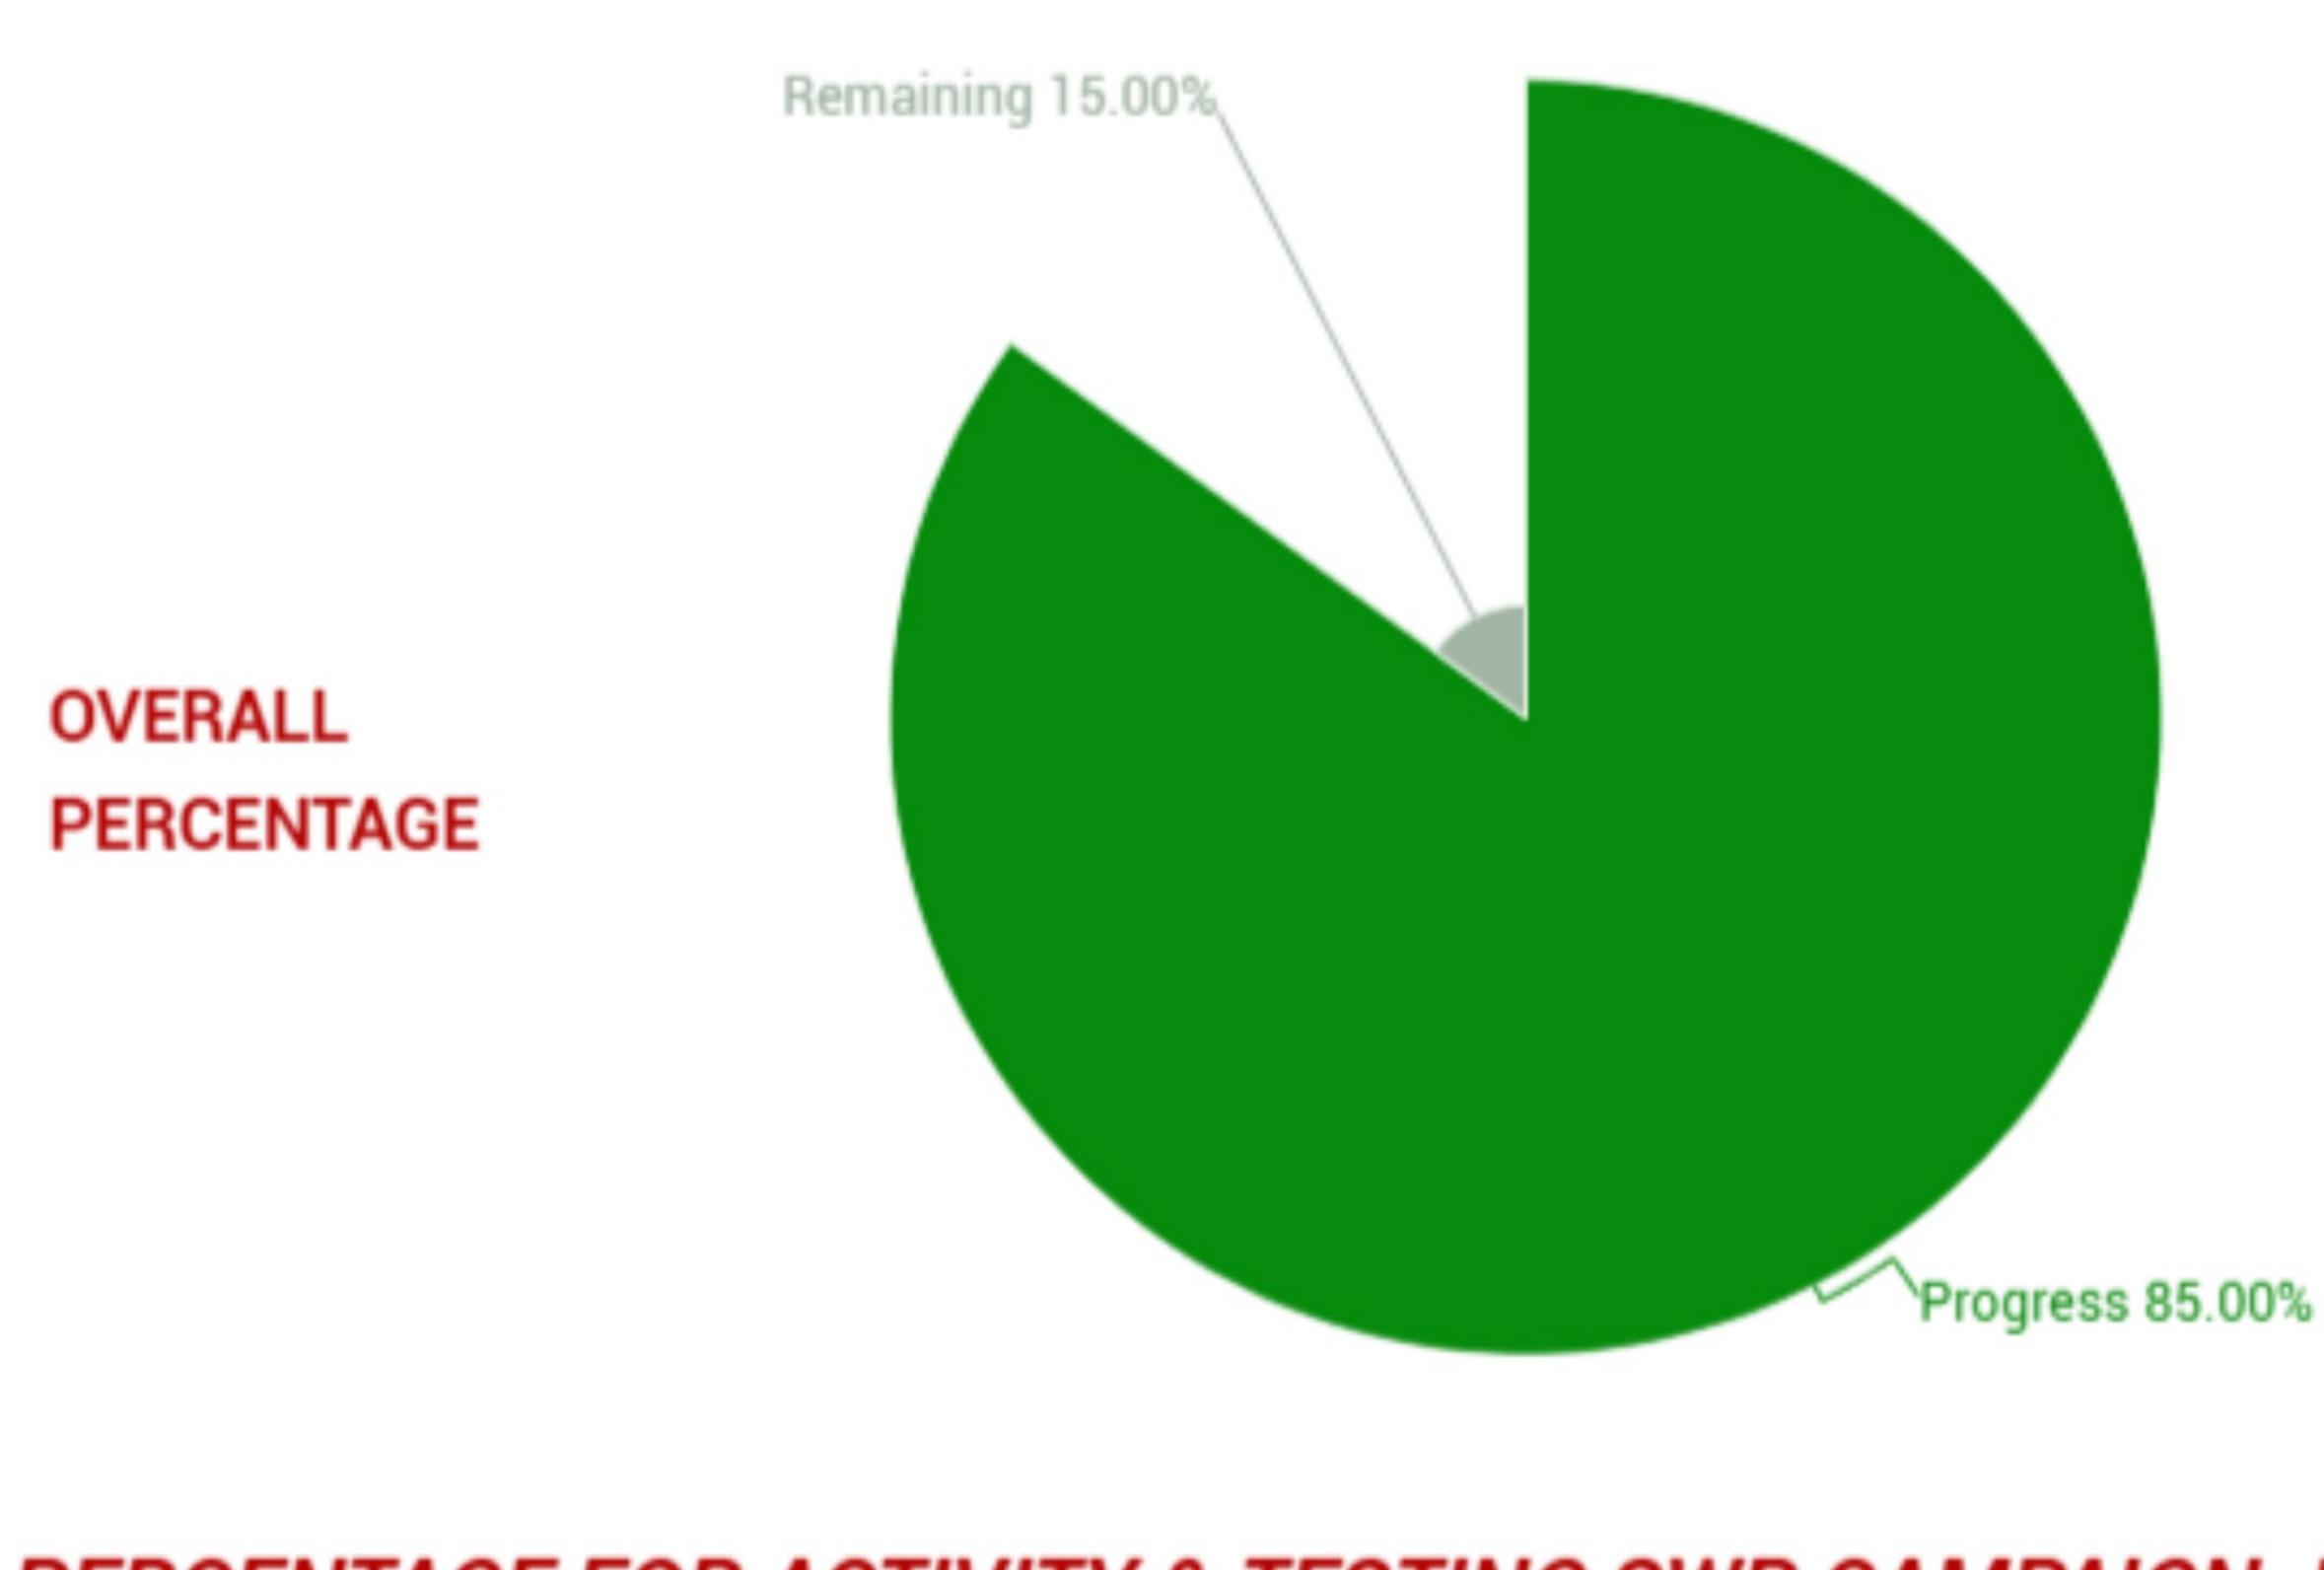

OVERALL PERCENTAGE FOR ACTIVITY & TESTING SWP CAMPAIGN JUNE 17<sup>th</sup>, 2023 - JUNE 24<sup>th</sup>, 2023

